

Conceptual Report	Preliminary Design	Detailed Design	Contract Documentation	Tender	Award	Construction 100%
-------------------	--------------------	-----------------	------------------------	--------	-------	--------------------------

CARP 2001 MONTANA Boland


A. PROJECT DETAILS

Community Access Roads Programme funded by the National Poverty Alleviation Fund

Implementing Agent: SANRAL
Project Value: R1 160 914
Project Type: Sidewalks/Safety
Consultant: ICE Group
 Mr Allan Truter
 Tel: 023 316 1063

Contractor: LCM Maintenance and Construction
 Mr L Abrahams
 Tel: 023 347 0910

Community Liaison Officer: Ricardo Fortuin
Training Coordinator: Mr M Fataar
 Tel: 021 447 9463


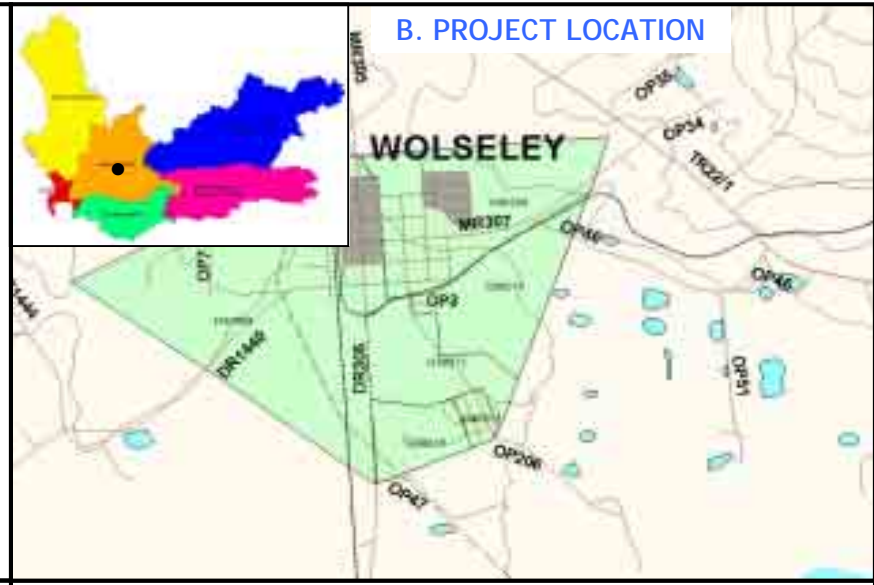


Community Information

Unemployed	845
Literacy age 14 and higher with grade 8 and higher	33%
Number of Households	611
Percentage of Households with income less than R1500/month	77%

F. JOB CREATION - Local Labour

Unemployed	No of Persons	Total Labour Days	Target Labour Days	Total Wage Expenditure
Men	12	2010	1421	R 130,925
Woman	7	1098	256	R 80,307
Youth (16-25)	9	1512	558	R 103,643
Disabled	1	229	100	R 34,973
Total	29	4849	2335	R 349,848

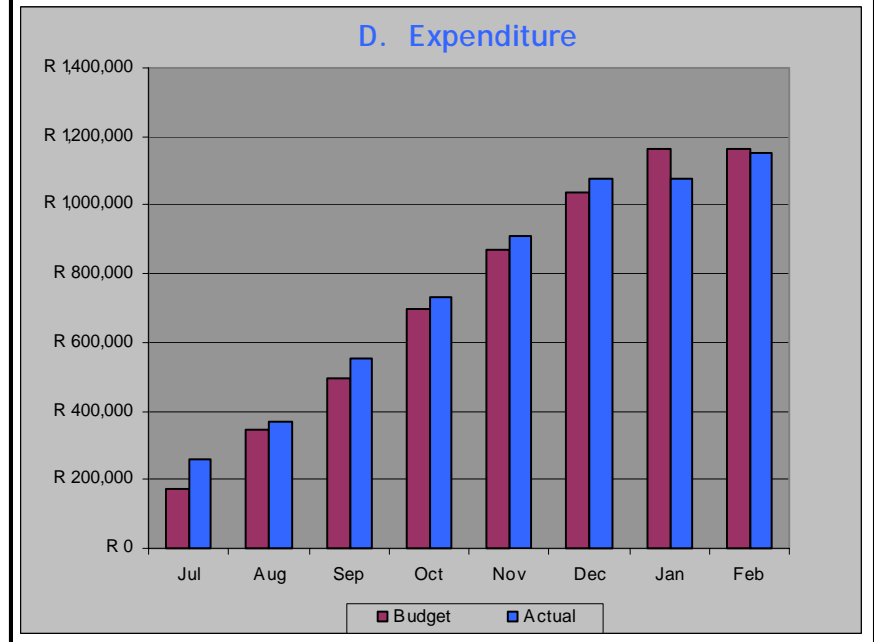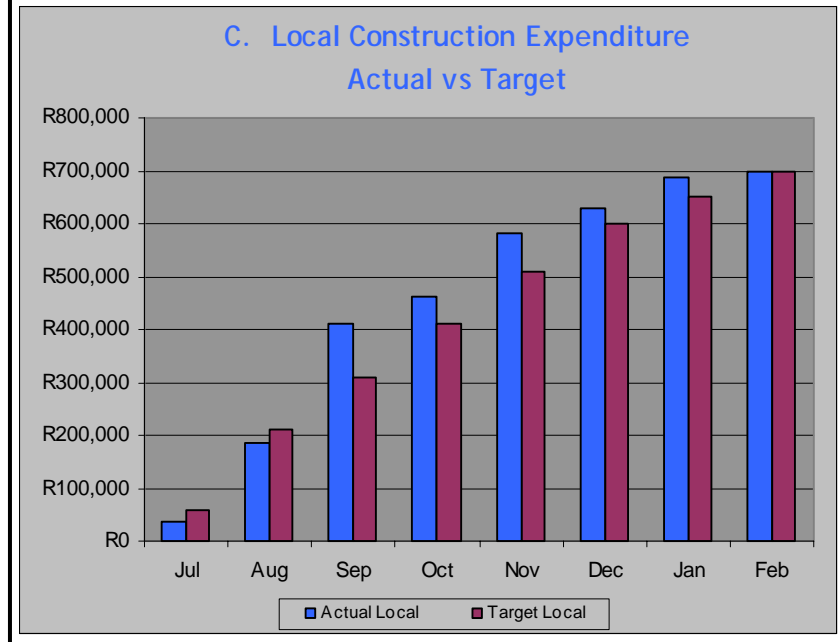

G. LOCAL LABOUR TRAINING

Unemployed	No of Persons	Total Labour Days	Total Wage Expenditure
Men	11	140	R 33,437
Woman	9	0	R 16,712
Youth (16-25)	11	70	R 25,090
Disabled	0	12	R 18,108
Total	31	222	R 43,212

H. AFFIRMABLE BUSINESS ENTERPRISES EMPLOYED

Name	Nature of Work	Total Expenditure (R)	Target (R)
LCM Construction	Main Contractor	R 898,242	R 898,242
			R 0
			R 0
			R 0
			R 0
Total		R 898,242	R 898,242

Main contractor is an ABE

E. Activities during construction



COMMUNITY FEEDBACK:

1. In general the community is happy with the procedures, quality and development of the project.

GENERAL COMMENTS:

1. The progress of the project is going as scheduled and no unfortunate incidents and disputes have been experienced yet

PROVINCIAL ADMINISTRATION OF THE WESTERN CAPE
 Department of Transport
 Community Based Public Works Programme



PROJECT NO: **NRA P04-001-00/1** COMPLETION: **FEB 2003**
